

BuyIt Software Development Plan: A C-BASS Component

by Dana L. Ulery, Brian R. Schallhorn, and Wade S. Jernigan

ARL-MR-443 May 1999

19990519 077

Approved for public release; distribution is unlimited.

The findings in this report are not to be construed as an official Department of the Army position unless so designated by other authorized documents.

Citation of manufacturer's or trade names does not constitute an official endorsement or approval of the use thereof.

Destroy this report when it is no longer needed. Do not return it to the originator.

Army Research Laboratory

Aberdeen Proving Ground, MD 21005-5067

ARL-MR-443 May 1999

BuyIt Software Development Plan: A C-BASS Component

Dana L. Ulery, Brian R. Schallhorn, and Wade S. Jernigan Corporate Information and Computing Center, ARL

Approved for public release; distribution is unlimited.

Abstract

A critical factor in the U.S. Army Research Laboratory's (ARL) strategy to do more with less resources is the automation of a single, ARL-wide purchasing process. This report describes the initial plan for developing the BuyIt Prototype, a software prototype for an automated purchasing system that provides an electronic workflow for ARL purchasing processes and interfaces with standard Department of Defense (DOD) systems required by those processes. The BuyIt Prototype is the first component of the Corporate Business Application Software System (C-BASS), a suite of integrated online transaction process software products that will provide Corporate business functions electronically throughout the ARL enterprise. C-BASS is a cornerstone of the new ARL Enterprise Information Technology Architecture developed in 1997 by the Enterprise Systems Division. This report provides a statement of the problem to be solved by the BuyIt Software, the technical and management approaches to be used, and a detailed project schedule.

Table of Contents

		Page
1.	Introduction	1
1.1	Identification	1
1.2	Purpose	1
1.3	Background	1
1.4	Organizational Responsibilities	2
1.4.1	Personnel Requirement	2
1.4.2	Interfacing Groups	2
2.	Statement of Problem	3
3.	Technical Approach	5
3.1	Life-Cycle Strategy	5
3.2	Assumptions and Constraints	5
3.3	Anticipated and Unresolved Problems	5
3.4	Development Environment	5
3.5	Activities, Tools, and Products	7
4.	Management Approach	7
4.1	Assumptions and Constraints	7
4.2	Resource Requirements	8
4.3	Milestones and Schedules	9
4.4	Metrics	9
4.5	Risk Management	9
5.	Product Assurance	10
5.1	Assumptions and Constraints	10
5.2	Quality Assurance	10
5.3	Configuration Management	10
6.	References	11
	Appendix: BuyIt Project Schedule	13
	Distribution List	17
	Report Documentation Page	19

List of Tables

<u>Table</u>		Page
1.	Project Personnel	3
2.	Interfacing Groups	3
3.	Prototype Assumptions	6
4.	Prototype Constraints	6
5.	Anticipated and Unresolved Problems	6
6.	Major Activities, Methodologies, and Products	7
7.	Distribution of Time Schedule and Effort Over Phases	8
8.	Project Team Training Requirements	8
9.	Key Project Metrics	9

1. Introduction

1.1 Identification. This report covers the plan for the development of BuyIt for use at the U.S. Army Research Laboratory (ARL) Adelphi Laboratory Center (ALC). This plan defines work that was begun in January 1997. Planning charts and activities described in the plan refer to the actual dates on which these project events were expected to occur.

The BuyIt Prototype forms the nucleus of BuyIt Version 1.0 for use at ALC as a full production system. BuyIt is a component of the Corporate Business Application Software System (C-BASS) family of applications, an integrated family of Notes and Web-based software to support ARL electronic workflow and task automation. This suite of applications interfaces with standard DOD systems to provide functionality unique to research and development (R&D) competencies.

- 1.2 Purpose. The purpose of the BuyIt Prototype is to experimentally model a secure client/server system that will provide for the automated routing, approval, tracking, and reporting of small purchase requests as part of the ARL Intranet. The proof-of-concept prototype is useful to mitigate risks by resolving unknowns related to new technologies being used to build the ARL Intranet architecture and to refine user requirements described by the Business Process Reengineering (BPR) "To-Be Model" [1].
- 1.3 Background. Initiation of this work is motivated by ARL downsizing and findings of the ARL BPR report on the small purchase process. It is the first business computing application identified for implementation as part of the new ARL Intranet.

ALC has been identified as the site with the most critical need for automated small purchase capability because it has had major reductions in purchasing staff and currently has no automated purchasing tools. The BPR "To-Be Model: Small Purchase" [1] identifies potential process improvements, some of which require computer-aided automation to increase efficiency of purchasing operations in ARL.

The full BuyIt Application System will implement a secure ARL-wide client/server system that allows users to:

- (1) Request small purchases electronically,
- (2) Route the request to the necessary functional users for electronic approval,
- (3) Automate interfaces to necessary standard legacy systems, and
- (4) Provide tracking and reporting and travel request status.

BuyIt will conform to the Enterprise Systems Division (ESD) life-cycle strategy for ARL Intranet application development. Development will be performed in phases, using an incremental, evolutionary approach. The first deliverable will be the BuyIt Prototype described in this plan.

The prototype will provide end-to-end functionality with scaled-down capabilities and will be usable only at ALC.

- 1.4 Organizational Responsibilities. The ARL Corporate Information and Computing Center (CICC) ESD has the responsibility to develop the BuyIt plan and system for all ARL sites. The Acting Chief of ESD is Dr. Dana Ulery.
- 1.4.1 Personnel Requirement. The prototype project team requires personnel from ESD, the Computing Support Branch (CSB) of CICC's Automation Resources Division, the Chief of Staff (COS) Procurement Office, and an outside contractor. Table 1 lists the project personnel and their responsibilities.
- 1.4.2 Interfacing Groups. The BuyIt project requires interfacing to user groups and to the CICC Advisory Committee. BuyIt users include COS personnel in procurement, budget, and logistics as well as scientists, engineers, managers, and administrative personnel at ALC who purchase items in this category.

Table 1. Project Personnel

Name	Org.	%	Responsibility
Wade Jernigan	ESD	75	Coleader, Development, Documentation
Brian Schallhorn	ESD	75	Coleader, Development, Documentation
Janet David	ESD	60	Testing, Documentation, CM, Metrics
John Leopard	ESD	100	Development, Documentation
Wendy McCoy	ESD	100	Development, Testing
Sr. Notes Developer (Contractor)	ProVar	100	Development, Documentation
Pam Stuecklen	CSB	10	Lotus Notes System Administration
Debbie Baggett	COS	5	User Requirements

Timely responsiveness of interface groups is critical to meeting the schedule for this project. Interface groups and the roles they play relative to this project are listed in Table 2.

Table 2. Interfacing Groups

Group	Org.	Role
Business Analysts	COS	Budget, Logistics, and Procurement process and data requirements
Standard Operations and Maintenance Army Research Development System (SOMARDS) User	COS	SOMARDS interface
Standard Army Automated Contracting System (SAACONS) User	COS	SAACONS interface
CICC Advisory Committee	CICC, Director's office, COS, directorates	User requirements, business direction

2. Statement of Problem

The prototype's key requirements are to provide the following automated functionalities:

- (1) Routing, approval, tracking, and reporting of small-purchase requests,
- (2) Funds certification through a SOMARDS interface, and
- (3) Upload of purchase request information into SAACONS.

Development of BuyIt Version 1 for full production use will be based on an evolutionary development approach that uses the Zachman architectural framework and an iterative, incremental life-cycle model [2, 3]. BuyIt Prototype Release 1 is the first intermediate product that will be developed on the path to developing BuyIt Version 1.

Four steps, each characterized by specific activities and the products produced by those activities, will be used to develop the prototype [4]:

- (1) Software requirements analysis,
- (2) Design analysis,
- (3) Implementation, and
- (4) System testing.

Deliverables will include:

- (1) Prototype software,
- (2) Prototype structured specifications document,
- (3) Prototype testing plans, and
- (4) Prototype user information sheet.

Intermediate software components produced to demonstrate specific functions will include:

- (1) Routing and tracking function,
- (2) Link to legacy systems, and
- (3) Reporting function.

The documents will provide precise, detailed technical models and processes, rather than ambiguous English-language descriptive text. They will be appropriately brief and, like the prototype software, form the nucleus for full system documentation [5].

3. Technical Approach

- 3.1 Life-Cycle Strategy. The life-cycle approach being used stresses three principles:
- (1) An architectural framework that explicitly defines critical system components from multiple perspectives and the relationships among these components in order to ensure integration of the business, operational, and computing models [6, 7];
- (2) Use of commercial-off-the-shelf products wherever possible to reduce costs and improve reliability and productivity [6, 7], and
- (3) Evolutionary, iterative steps to incrementally build multiple, shorter-cycle products and control risk [6, 7].

The prototype is the first phase in the life cycle of the full production product.

- 3.2 Assumptions and Constraints. Some of the key assumptions and constraints are shown in Tables 3 and 4, but the lists are not all-inclusive.
- 3.3 Anticipated and Unresolved Problems. Table 5 lists some of the anticipated and unresolved problems that could affect the prototype development and delivery.
 - 3.4 Development Environment. The development environment will consist of:
 - Hardware
 - Server: PC, dual 133-MHz Pentium processors, 96 MB RAM, (2) 4.5-GB hard drives, 4X CD-ROM, 4-GB 4-mm tape drive, ethernet.
 - Client development: PCs, Pentium.

Table 3. Prototype Assumptions

Assumption	Explanation
13 January 1997 - Project Start Date	Requires that the ALC Lotus Notes development server is installed, tested, and operational by that date. If not, start date must be delayed until these conditions are satisfied.
User requirements for prototype are frozen	Will be based primarily on the BPR "To-Be Model."
Prototype will not be used for critical operations	Prototypes are experimental models lacking the completeness and robustness of full production systems.

Table 4. Prototype Constraints

Constraint	Explanation
Incomplete user requirements analysis	Details of user requirements needed for software analysis will not be done for prototype.
ALC site only	Practices differ among sites, limiting complexity of business model.
Single product category	The requester may only purchase items that either (1) require no special approvals or (2) require special approval through only one designated office (TBD). This simplifies the automated special approval process.
Single vender per request	The requester may enter three suggested vendors, but they must be for all the items on the request. Separate items may not go to separate vendors. Simplifies the interface to SAACONS.
No requester credit card capability	All requests must go through the full procurement cycle. Procurement buyers may use credit cards.

Table 5. Anticipated and Unresolved Problems

Problem	Details
Skill gaps	Project developers from ESD have very limited Lotus Notes experience and few software engineering skills. Personnel from Systems Operations Branch (SOB) have very limited experience administering Lotus Notes.
Hardware	 New Lotus Notes servers not fully tested in ARL development environment. New development client hardware required for this project not yet tested in ARL development environment.
Legacy systems	 Need for middleware products between Notes and the legacy systems (SOMARDS and SAACONS) not yet resolved. SOMARDS function is moving to Rock Island, IL, severely restricting ARL access to SOMARDS systems personnel necessary to support any special input/output (I/O) or interface needs.

• Software

- Server: Microsoft Windows NT Server v4.0 w/Lotus Notes Server v4.5.
- Client development: Microsoft Windows 95 or NT Workstation v4.0 w/Lotus Notes Desktop v4.5.
- Middleware between Lotus Notes and the legacy system (TBD).
- 3.5 Activities, Tools, and Products. Table 6 lists the major activities, methodologies, and tools to be used and the products of each phase during the prototype development cycle.

Table 6. Major Activities, Methodologies, and Products

Activity	Methodology/Tools	Products
Software Requirements Analysis	Structured analysis [4]	Data flow modelData modelStructured specifications document
Design Analysis	Structured design [8, 5]	Legacy interfacesForms designNavigators designStructure charts
Implementation	Lotus Notes application development [9]	 Routing and tracking function Link to legacy systems Reporting function Prototype software
System Testing	 Software engineering testing methods and tools Configuration management 	 Prototype test plan Inspection summaries Test logs Discrepancy reports Configuration management controls

4. Management Approach

4.1 Assumptions and Constraints. Lack of experience with Lotus Notes application development and the new C-BASS computing environment combine to maximize the software engineering complexity rating for this project. The less than 2 years of experience, on average,

with the project technologies increases the uncertainty of effort estimate by a factor greater than 2.

This circumstance also is reflected in the projected schedule of activities and milestones. For example, training will have a high priority during the initial stages of the project.

Factors of resource scheduling also impact the development timeline given in this report. While the BuyIt Prototype has a high priority for ESD, it must compete with other high-priority tasks associated with establishing the ARL Intranet. Three project personnel from ESD, including both coleaders, are responsible for and are working on other assignments in parallel with their work on this project.

4.2 Resource Requirements. Estimates of the distribution of time schedule and effort over the development phases are listed in Table 7. Estimates of formal training requirements for project team members are shown in Table 8.

Table 7. Distribution of Time Schedule and Effort Over Phases

Phase	Time Schedule (%)	Effort (%)
Software Requirements Analysis	15	12
Design Analysis	25	33
Implementation	45	40
System Testing	15	15

Table 8. Project Team Training Requirements

Course	Time Schedule (%)	Total (Weeks)
Lotus Notes Application Dev. II	5	3
Advanced Lotus Notes	3	1.5

- 4.3 Milestones and Schedules. Appendix A gives the detailed schedule for this project, showing work breakdowns, task duration, start and end dates, task dependencies, and milestones (based on the received guidance for the project start). Significant milestones include:
 - Installing the hardware and software making up the development environment,
 - Completing software requirements analysis,
 - Defining system architecture, data description, user interface, and processing actions,
 - · Implementing software designs and link to legacy system, and
 - Bench-testing and field-testing the prototype.
- **4.4 Metrics.** Metrics will be used to monitor and manage progress and product quality. Both objective and subjective data will be used to get a picture of project status. Key project metrics and their uses are listed in Table 9.

Table 9. Key Project Metrics

Metric	Frequency	Use	
Development task status	Weekly	Progress, process control, design stability	
Changes (to specs, design)	Biweekly	Quality of specs, design; identify need to iterate an earlier phase	
Software size estimates	Biweekly	Progress; quality of process and design	
Tests	Weekly	Progress; quality of software, design	

4.5 Risk Management. The primary tool for managing risk is the use of disciplined software engineering approaches and methods [6, 7]. As mentioned elsewhere in this plan, the use of multiple new technologies coupled with an inexperienced staff makes this a project subject to risk. The detailed technical models being developed in all phases of the project provide a basis for assessing technical risk. Potentially high-risk conditions, whether technical or nontechnical, will be identified promptly and brought to the attention of the managers responsible for decisions regarding project resources and timing.

5. Product Assurance

- **5.1** Assumptions and Constraints. The BuyIt Prototype is a proof-of-concept model and is not intended for use in a production environment or as a tool to replace a critical manual system.
- 5.2 Quality Assurance. Monthly 2-hour reviews will be held at ALC with management from CICC, COS, and the CICC Advisory Committee to assess the condition of the project. The reviews will provide regularly scheduled monitoring of project status. They will address quality assurance by examining the plans, milestones, and intermediate products associated with the development process.

The first review is scheduled for the morning of 4 February 1997, subject to the 13 January starting date.


- **5.3 Configuration Management.** Standard Configuration Management (CM) methodology will be used to control changes to system products. The following list gives the prototype products that will be under CM control:
 - (1) Product Software,
 - (2) Software Development Plan,
 - (3) Software Requirements Analysis Document,
 - (4) Data Flow Model,
 - (5) Data Model,
 - (6) Design Document,
 - (7) Test Plan, and
 - (8) Test Reports.


6. References

- 1. U.S. Army Research Laboratory. *To-Be Model: Small Purchase*. Business Process Reengineering Project, Aberdeen Proving Ground, MD, July 1995.
- 2. Zachman, J. A. "A Framework for Information Systems Architecture." *IBM Systems Journal*, vol. 26, no. 3, 1987.
- 3. Sowa, J. F., and J. A. Zachman. "Extending and Formalizing the Framework for Information Systems Architecture." *IBM Systems Journal*, vol. 31, no. 3, 1992.
- 4. Yourdon, E. Modern Structured Analysis. Englewood Cliffs, NJ: Yourdon Press, 1989.
- 5. Page-Jones, M. The Practical Guide to Structured Systems Design. Englewood Cliffs, NJ: Yourdon Press, 1988.
- 6. Landis, L. (ed.). Manager's Handbook for Software Development Revision 1. SEL-84-101, Software Engineering Laboratory, College Park, MD, 1990.
- 7. Landis, L., S. Waligora, F. McGarry, R. Pajerski, M. Stark, K. O. Johnson, and D. Cover. Recommended Approach to Software Development Revision 3. Software Engineering Laboratory, SEL-81-305, College Park, MD, 1992.
- 8. DeMarco, T. Concise Notes on Software Engineering. Englewood Cliffs, NJ: Yourdon Press, 1979.
- 9. Lotus Development Corporation. "Lotus Notes Release 4: Application Development." Student Guide, Cambridge, MA, 1996.

Appendix:

BuyIt Project Schedule

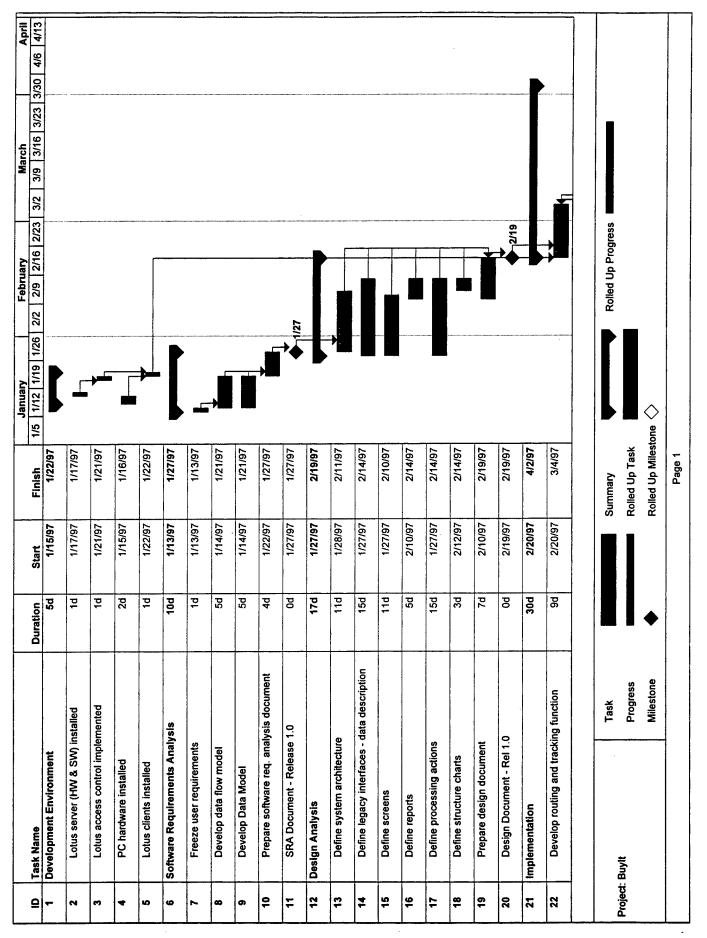

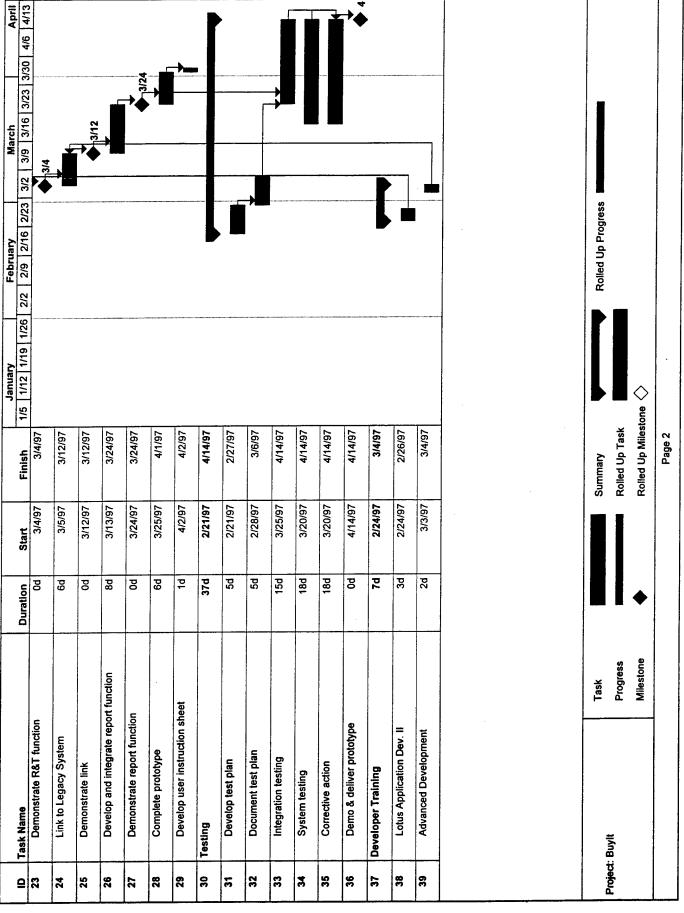

NO. OF COPIES ORGANIZATION

- 2 DEFENSE TECHNICAL INFORMATION CENTER DTIC DDA 8725 JOHN J KINGMAN RD STE 0944 FT BELVOIR VA 22060-6218
- 1 HQDA
 DAMO FDQ
 D SCHMIDT
 400 ARMY PENTAGON
 WASHINGTON DC 20310-0460
- 1 OSD
 OUSD(A&T)/ODDDR&E(R)
 R J TREW
 THE PENTAGON
 WASHINGTON DC 20301-7100
- 1 DPTY CG FOR RDE HQ
 US ARMY MATERIEL CMD
 AMCRD
 MG CALDWELL
 5001 EISENHOWER AVE
 ALEXANDRIA VA 22333-0001
- 1 INST FOR ADVNCD TCHNLGY THE UNIV OF TEXAS AT AUSTIN PO BOX 202797 AUSTIN TX 78720-2797
- 1 DARPA B KASPAR 3701 N FAIRFAX DR ARLINGTON VA 22203-1714
- 1 NAVAL SURFACE WARFARE CTR CODE B07 J PENNELLA 17320 DAHLGREN RD BLDG 1470 RM 1101 DAHLGREN VA 22448-5100
- 1 US MILITARY ACADEMY
 MATH SCI CTR OF EXCELLENCE
 DEPT OF MATHEMATICAL SCI
 MAJ M D PHILLIPS
 THAYER HALL
 WEST POINT NY 10996-1786

NO. OF COPIES ORGANIZATION

- DIRECTOR
 US ARMY RESEARCH LAB
 AMSRL D
 R W WHALIN
 2800 POWDER MILL RD
 ADELPHI MD 20783-1145
- 1 DIRECTOR
 US ARMY RESEARCH LAB
 AMSRL DD
 J J ROCCHIO
 2800 POWDER MILL RD
 ADELPHI MD 20783-1145
- 1 DIRECTOR
 US ARMY RESEARCH LAB
 AMSRL CS AS (RECORDS MGMT)
 2800 POWDER MILL RD
 ADELPHI MD 20783-1145
- 3 DIRECTOR
 US ARMY RESEARCH LAB
 AMSRL CI LL
 2800 POWDER MILL RD
 ADELPHI MD 20783-1145

ABERDEEN PROVING GROUND

4 DIR USARL AMSRL CI LP (305)

NO. OF COPIES ORGANIZATION

- 1 DIRECTOR
 US ARMY RESEARCH LAB
 AMSRL PP B M FONOROF
 2800 POWDER MILL RD
 ADELPHI MD 20783-1145
- 2 DIRECTOR
 US ARMY RESEARCH LAB
 AMSRL CI E
 B R SCHALLHORN
 W S JERNIGAN
 2800 POWDER MILL RD
 ADELPHI MD 20783-1145

ABERDEEN PROVING GROUND

2 DIR USARL

AMSRL CI

C J NIETUBICZ

AMSRL CI E

D L ULERY

REPORT DO	Form Approved OMB No. 0704-0188			
Public reporting burden for this collection of informs gathering and maintaining the data needed, and com				
collection of information, including suggestions for in Davis Highway, Suite 1204, Artington, VA 22202-4302	reducing this burden, to washington Headquarters : 2. and to the Office of Management and Budget. Pag		Vashington, DC 20503.	
1. AGENCY USE ONLY (Leave blank)	2. REPORT DATE May 1999	Final, 10 December		
4. TITLE AND SUBTITLE	Iviay 1999		5. FUNDING NUM	
BuyIt Software Development P	lan: A C-BASS Component		9UA4EC	
6. AUTHOR(S)			JUN4DC	
Dana L. Ulery, Brian R. Schalll	horn, and Wade S. Jernigan			
7. PERFORMING ORGANIZATION NAM			B. PERFORMING	ORGANIZATION
7. PERFORMING ORGANIZATION NAM			REPORT NUM	BER
U.S. Army Research Laborator	у	ŀ	ARL-MR-	443
ATTN: AMSRL-CI-E	21005 5067	ĺ	LTIN-TATIO	
Aberdeen Proving Ground, MD	21003-300/			
9. SPONSORING/MONITORING AGEN	CY NAMES(S) AND ADDRESS(ES)		10.SPONSORING	MONITORING PORT NUMBER
11. SUPPLEMENTARY NOTES				
•				
12a. DISTRIBUTION/AVAILABILITY ST	ATEMENT		12b. DISTRIBUT	ION CODE
Approved for public release; di	istribution is unlimited.			
rippiovod for public resources, and		•		
13. ABSTRACT (Maximum 200 words)	J.S. Army Research Laborator	v's (ARL) strategy to	do more with	less resources is the
automation of a single ARI -v	wide purchasing process. This	report describes the in	utial plan for	developing the Buyit
Prototype a software prototy	ne for an automated purchasir	ng system that provide:	s an electron	ic worktion for AIRL
nurchasing processes and inter	rfaces with standard Departmen	at of Defense (DOD) sy	stems require	ed by mose processes.
The BuyIt Prototype is the first	t component of the Corporate E	Business Application So	itware System	n (C-BASS), a suite of
integrated online transaction p throughout the ARL enterpri	process software products that	will provide Corporation of the new ARI.	e ousmess n Interprise Inf	formation Technology
Architecture developed in 199	Se. C-BASS is a confession 7 by the Enterprise Systems Di	vision. This report pro	vides a stater	nent of the problem to
he solved by the BuyIt Softwar	re, the technical and manageme	nt approaches to be use	d, and a detai	led project schedule.
00 001100 09 0.0 20920 002	 ,	••		
44 OUR IDOT TERMS			15. N	JMBER OF PAGES
14. SUBJECT TERMS				20
BuyIt, software development p	plan, software development, C-l	BASS, purchasing appli	cation 16. Pl	RICE CODE
17. SECURITY CLASSIFICATION	18. SECURITY CLASSIFICATION	19. SECURITY CLASSIFIC	ATION 20. LI	MITATION OF ABSTRACT
OF REPORT	OF THIS PAGE	OF ABSTRACT		
UNCLASSIFIED	UNCLASSIFIED	UNCLASSIFIE	<u> </u>	SAR

USER EVALUATION SHEET/CHANGE OF ADDRESS

This Laboratory undertakes a continuing effort to improve the quality of the reports it publishes. Your comments/answers to the items/questions below will aid us in our efforts.

1. ARL Report Numb	per/Author ARL-MR-443 (Ulery	Date of Report May 1999
2. Date Report Recei	ved	
	tisfy a need? (Comment on purpose,	related project, or other area of interest for which the report will
		n source, design data, procedure, source of ideas, etc.)
5. Has the information	on in this report led to any quantitativ	re savings as far as man-hours or dollars saved, operating costs ate.
technical content, for		ed to improve future reports? (Indicate changes to organization,
	Organization	
CURRENT ADDRESS	Name	E-mail Name
	Street or P.O. Box No.	
	City, State, Zip Code	And the state of t
7. If indicating a Char or Incorrect address b	~	please provide the Current or Correct address above and the Old
	Organization	
OLD ADDRESS	Name	
	Street or P.O. Box No.	
	City, State, Zip Code	
	•	indicated, tape closed, and mail.) T STAPLE)
